


MB-01

Lost Creek ISR, LLC
WELL COMPLETION REPORT

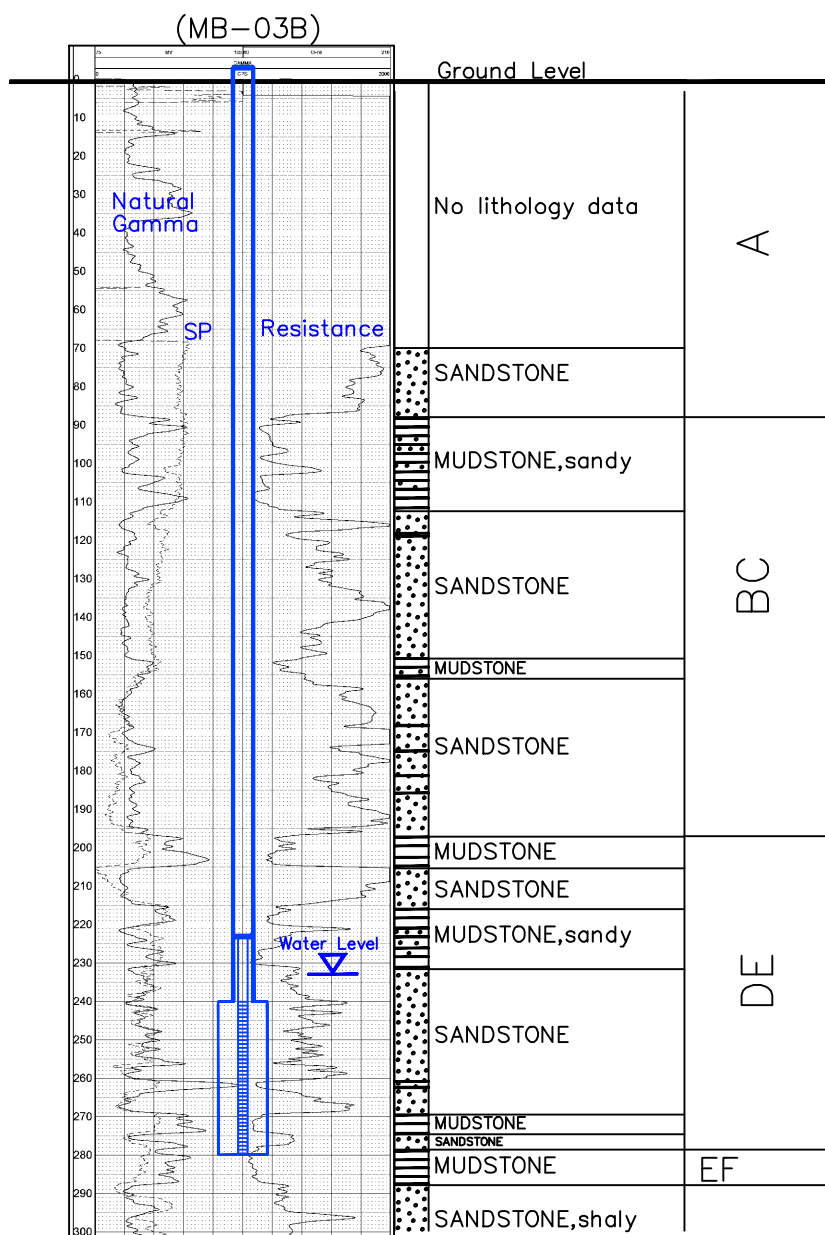

Vertical Scale: 1"=50'

NOTE: MB-01 was drilled with air. Hole made no water. Hole not logged. Log for MB-03B used here as representative.

WELL # MB-01 SEO # 188852 Date Drilled: 10-6-08

Location: E 736,248 / N 535,851 (NAD 27)

Ground Elev: 6984.39 Measure Point Elev: 6985.89

TD: 300 ft. Hole Dia.: 7-7/8"

CASED to: 240' Casing: PVC SDR17 ID: 4.5" OD: 5"

GROUT: Portland Cement – Type I/II
Pumped thru casing, displaced to surface with water

COMPLETION Aquifer: DE Sand

Static Water Level: Depth 233' Elev: 6752' (avg.)

UNDERREAM: Blade Dia: 10-1/2"

Intervals: from 240' to 280' /length 40'

from _____ to _____ /length _____

SCREEN LINER ASSEMBLY

Description	Depth		Elev.		Length
	From	To	From	To	
K-packer		233'		6752'	
Screen	240'	280'	6745'	6705'	40'

SCREEN SPECIFICATIONS:

Slot: 0.020" Composition 3" PVC

FILTER PACKING:

Volume: _____ (bags)(ft³) Sand Specs. _____

Method: N/A

WELL STIMULATION: Method Airlift

Yield: Good / Moderate / Poor
