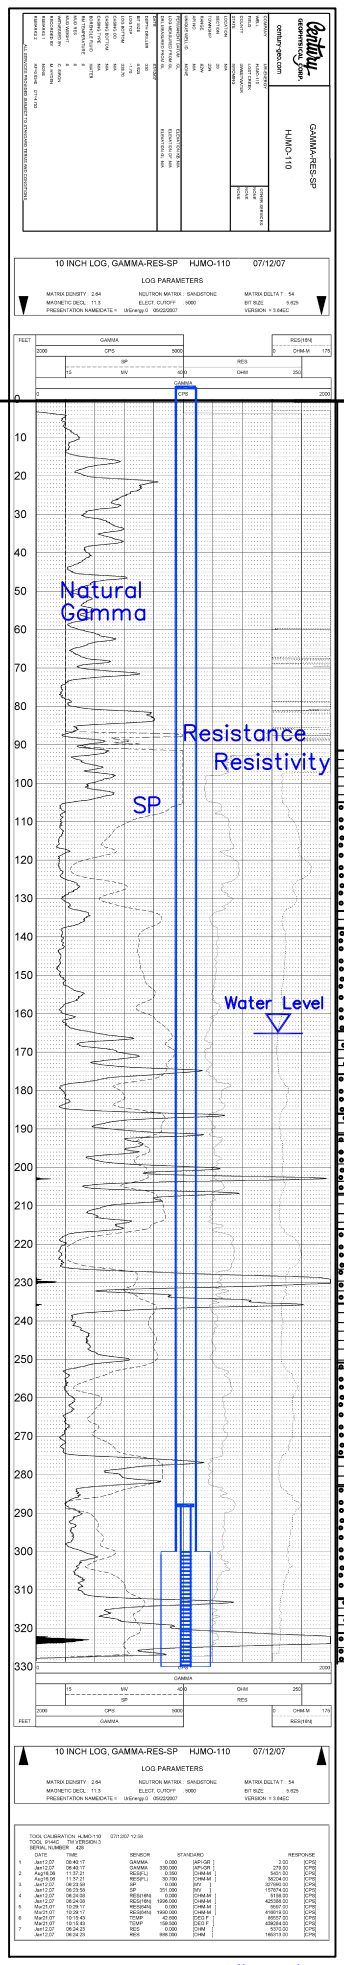

Vertical Scale: 1"=50'

HJMO–110

Lost Creek ISR, LLC

WELL COMPLETION REPORT

WELL # HJMO–110 SEO # 179892 Date Drilled: 7–12–07

Location: E 743,675 / N 535,194 (NAD 27)

Ground Elev: 6945.92' Measure Point Elev: 6947.13'

TD: 330' Hole Dia.: 7–7/8"

CASED to: 300' Casing: PVC SDR17 ID: 4.5" OD: 5"

GROUT: Portland Cement – Type I/II
Pumped thru casing, displaced to surface with water

COMPLETION Aquifer: LFG Sand

Static Water Level: Depth 165' Elev: 6782' (avg.)

UNDERREAM: Blade Dia: 10.5"

Intervals: from 300' to 330' /length 30'

from _____ to _____ /length _____

SCREEN LINER ASSEMBLY

Description	Depth From – To	/ Elev. From – To	Length
K–packer	288'	6659'	
Screen	300' – 330'	6647' – 6617'	30'

SCREEN SPECIFICATIONS:

Slot: 0.030" Composition 3" PVC

FILTER PACKING:

Volume: _____(bags)(ft^3) Sand Specs. _____

Method: N/A

WELL STIMULATION: Method Airlift

Yield: Good / Moderate / (Poor)
