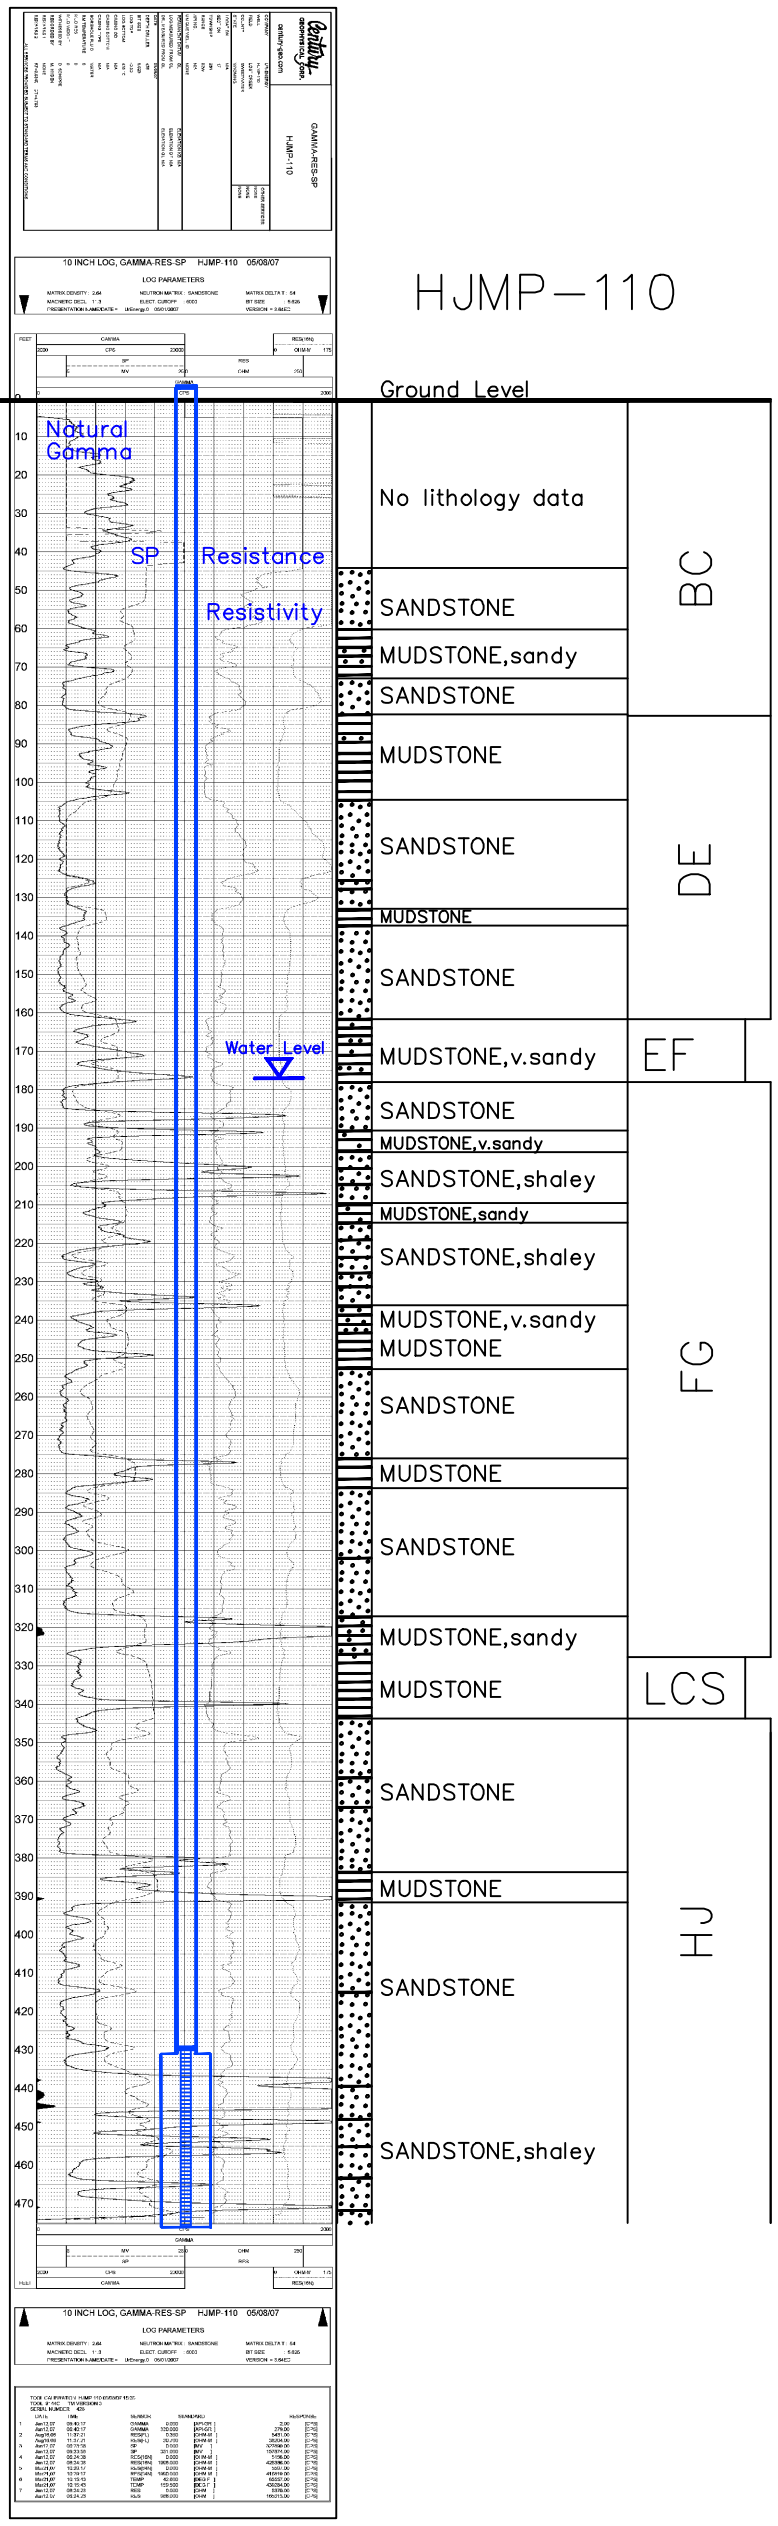

Vertical Scale: 1"=50'

HJMP–110

Lost Creek ISR, LLC

WELL COMPLETION REPORT

WELL # HJMP–110 SEO # 179891 Date Drilled: 5–8–07

Location: E 743,682 / N 535,184 (NAD 27)

Ground Elev: 6945.81' Measure Point Elev: 6947.01'

TD: 476' Hole Dia.: 7–7/8"

CASED to: 431' Casing: PVC SDR17 ID: 4.5" OD: 5"

GROUT: Portland Cement – Type I/II
Pumped thru casing, displaced to surface with water

COMPLETION Aquifer: HJ Sand

Static Water Level: Depth 177' Elev: 6770' (avg.)

UNDERREAM: Blade Dia: 10.5"

Intervals: from 431' to 476' /length 45'

from _____ to _____ /length _____

SCREEN LINER ASSEMBLY

Description	Depth From – To		Elev. / From – To		Length
K–packer		430'		6517'	
Screen	431'	476'	6516'	6471'	45'

SCREEN SPECIFICATIONS:

Slot: 0.020" Composition 3" PVC

FILTER PACKING:

Volume: _____ (bags)(ft^3) Sand Specs. _____

Method: N/A

WELL STIMULATION: Method Airlift

Yield: (Good) / Moderate / Poor
