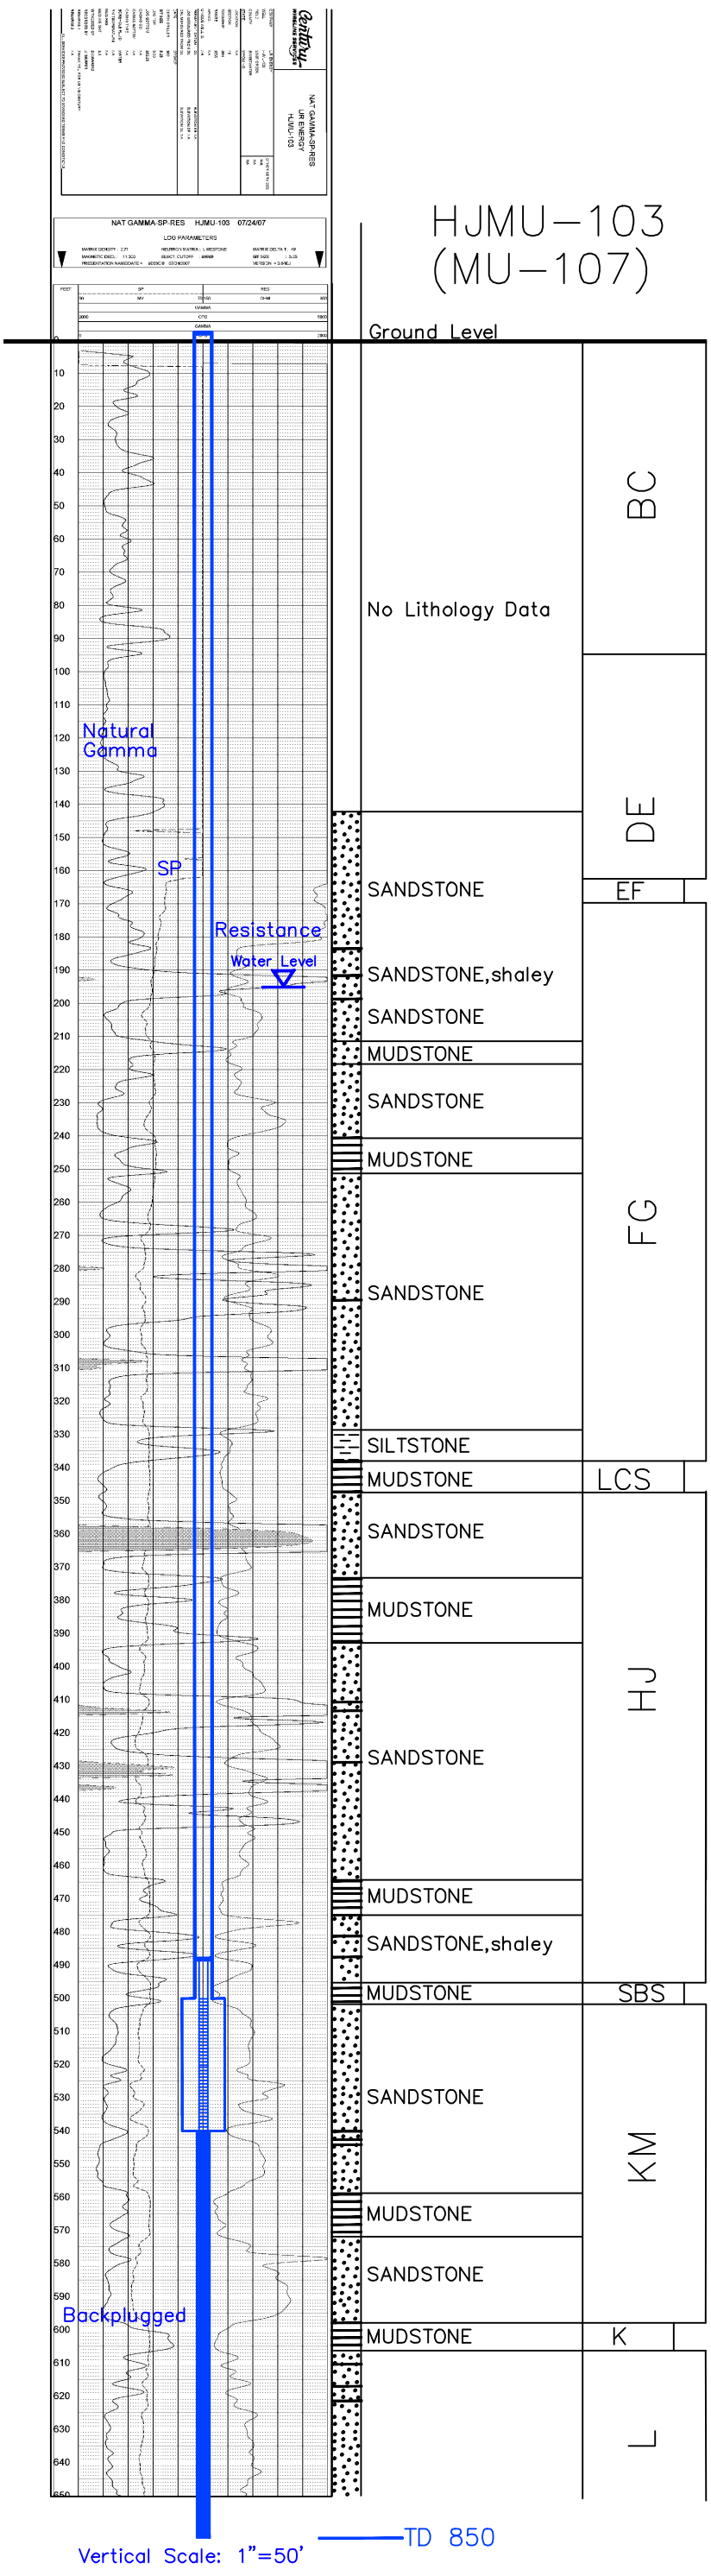

Lost Creek ISR, LLC

WELL COMPLETION REPORT

WELL # HJMU-103 SEO # 179869 Date Drilled: 7-24-07

Location: E 742,657 / N 535,098 (NAD 83)

Ground Elev: 6935.06 Measure Point Elev: 6936.06

TD: 850 ft. Hole Dia.: 7-7/8"

CASED to: 500' Casing: PVC SDR17 ID: 4.5" OD: 5"

GROUT: Portland Cement – Type I/II
Pumped thru casing, displaced to surface with water

COMPLETION Aquifer: UKM Sand

Static Water Level: Depth 195' Elev: 6741'

UNDERREAM: Blade Dia: 10-1/2"

Intervals: from 500' to 540' /length 40'

from _____ to _____ /length _____

SCREEN LINER ASSEMBLY

Description	Depth From	– To	/ Elev. From	– To	Length
K-packer		488'		6448'	
Screen	500'	540'	6436'	6396'	40'

SCREEN SPECIFICATIONS:

Slot: 0.020" Composition 3" PVC

FILTER PACKING:

Volume: _____ (bags)(ft^3) Sand Specs. _____

Method: N/A

WELL STIMULATION: Method Airlift

Yield: (Good) / Moderate / Poor

Pilot Hole BACKPLUGGED: 540'–850'

w/ BH Ultragrout slurry – 25% solids
