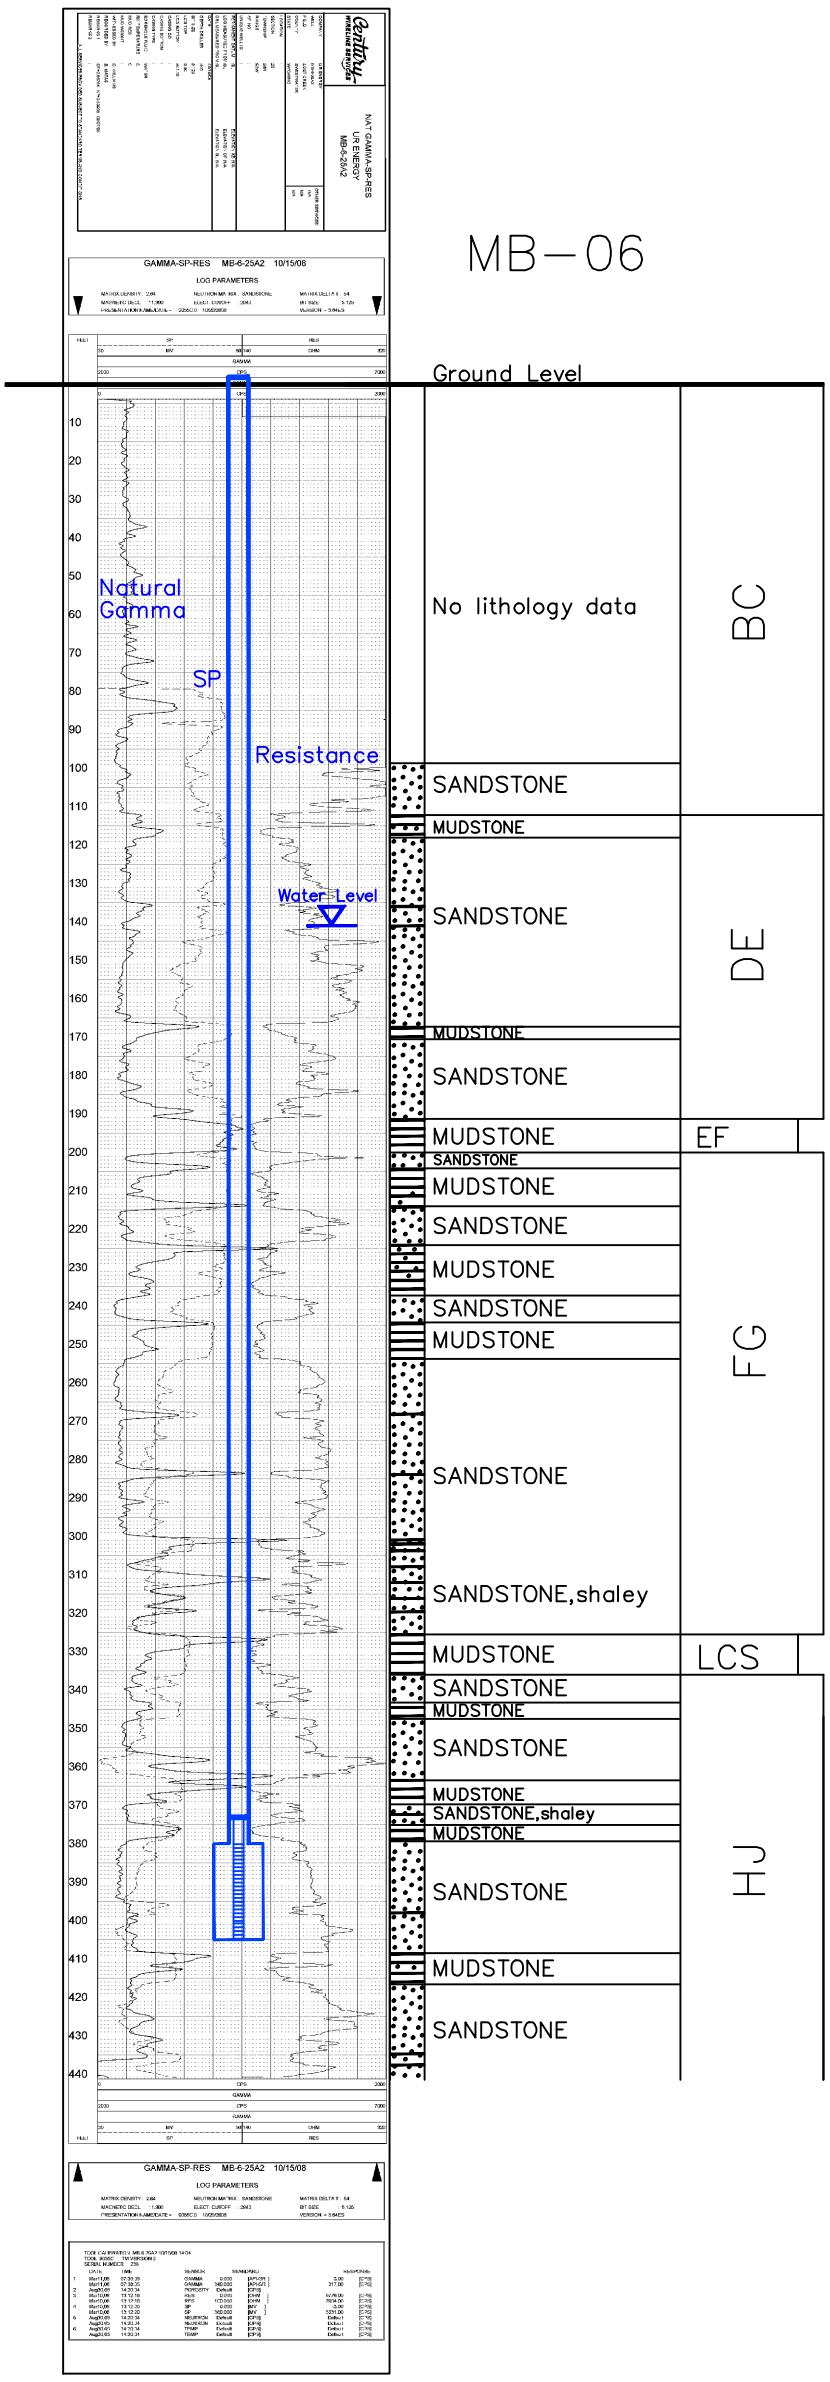

Vertical Scale: 1"=50'

MB-06

Lost Creek ISR, LLC

WELL COMPLETION REPORT

WELL # MB-06 SEO # 188857 Date Drilled: 10-15-08

Location: E 733,376 / N 524,466 (NAD 27)

Ground Elev: 6803.40' Measure Point Elev: 6804.90'

TD: 440' Hole Dia.: 7-7/8"

CASED to: 380' Casing: PVC SDR17 ID: 4.5" OD: 5"

GROUT: Portland Cement – Type I/II
Pumped thru casing, displaced to surface with water

COMPLETION Aquifer: HJ Sand

Static Water Level: Depth 141' Elev: 6664' (avg.)

UNDERREAM: Blade Dia: 10.5"

Intervals: from 380' to 405' /length 25'

from _____ to _____ /length _____

SCREEN LINER ASSEMBLY

Description	Depth From – To		Elev. From – To		Length
K-packer		373'		6432'	
Screen	380'	405'	6425'	6400'	25'

SCREEN SPECIFICATIONS:

Slot: 0.020" Composition 3" PVC

FILTER PACKING:

Volume: _____ (bags)(ft^3) Sand Specs. _____

Method: N/A

WELL STIMULATION: Method Airlift

Yield: (Good) / Moderate / Poor
