HJMO–114
(MO–102)

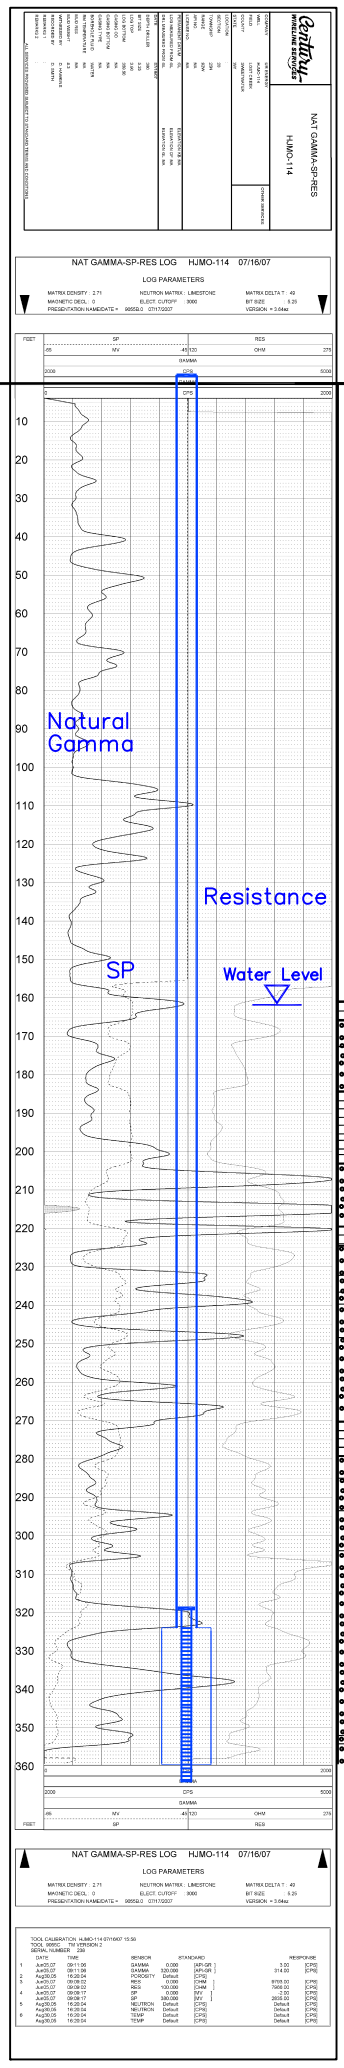

Vertical Scale: 1"=50'

HJMO–114
(MO–102)

Lost Creek ISR, LLC

WELL COMPLETION REPORT

WELL # HJMO–114 SEO # 179904 Date Drilled: 7–16–07

Location: E 744,979 / N 534,676 (NAD27)

Ground Elev: 6939.09' Measure Point Elev: 6940.75'

TD: 364' Hole Dia.: 7–7/8"

CASED to: 324' Casing: PVC SDR17 ID: 4.5" OD: 5"

GROUT: Portland Cement – Type I/II
Pumped thru casing, displaced to surface with water

COMPLETION Aquifer: LFG Sand

Static Water Level: Depth 162' Elev: 6779' (Avg)

UNDERREAM: Blade Dia: 10.5"

Intervals: from 324' to 360' /length 36'

from _____ to _____ /length _____

SCREEN LINER ASSEMBLY

Description	Depth From – To		Elev. / From – To		Length
K–packer		319'		6622'	
Screen	324'	364'	6617'	6577'	30'

SCREEN SPECIFICATIONS:

Slot: 0.030" Composition 3" PVC

FILTER PACKING:

Volume: _____ (bags)(ft^3) Sand Specs. _____

Method: N/A

WELL STIMULATION: Method Airlift

Yield: Good / (Moderate) / Poor

HJMO–114
(MO–102)
