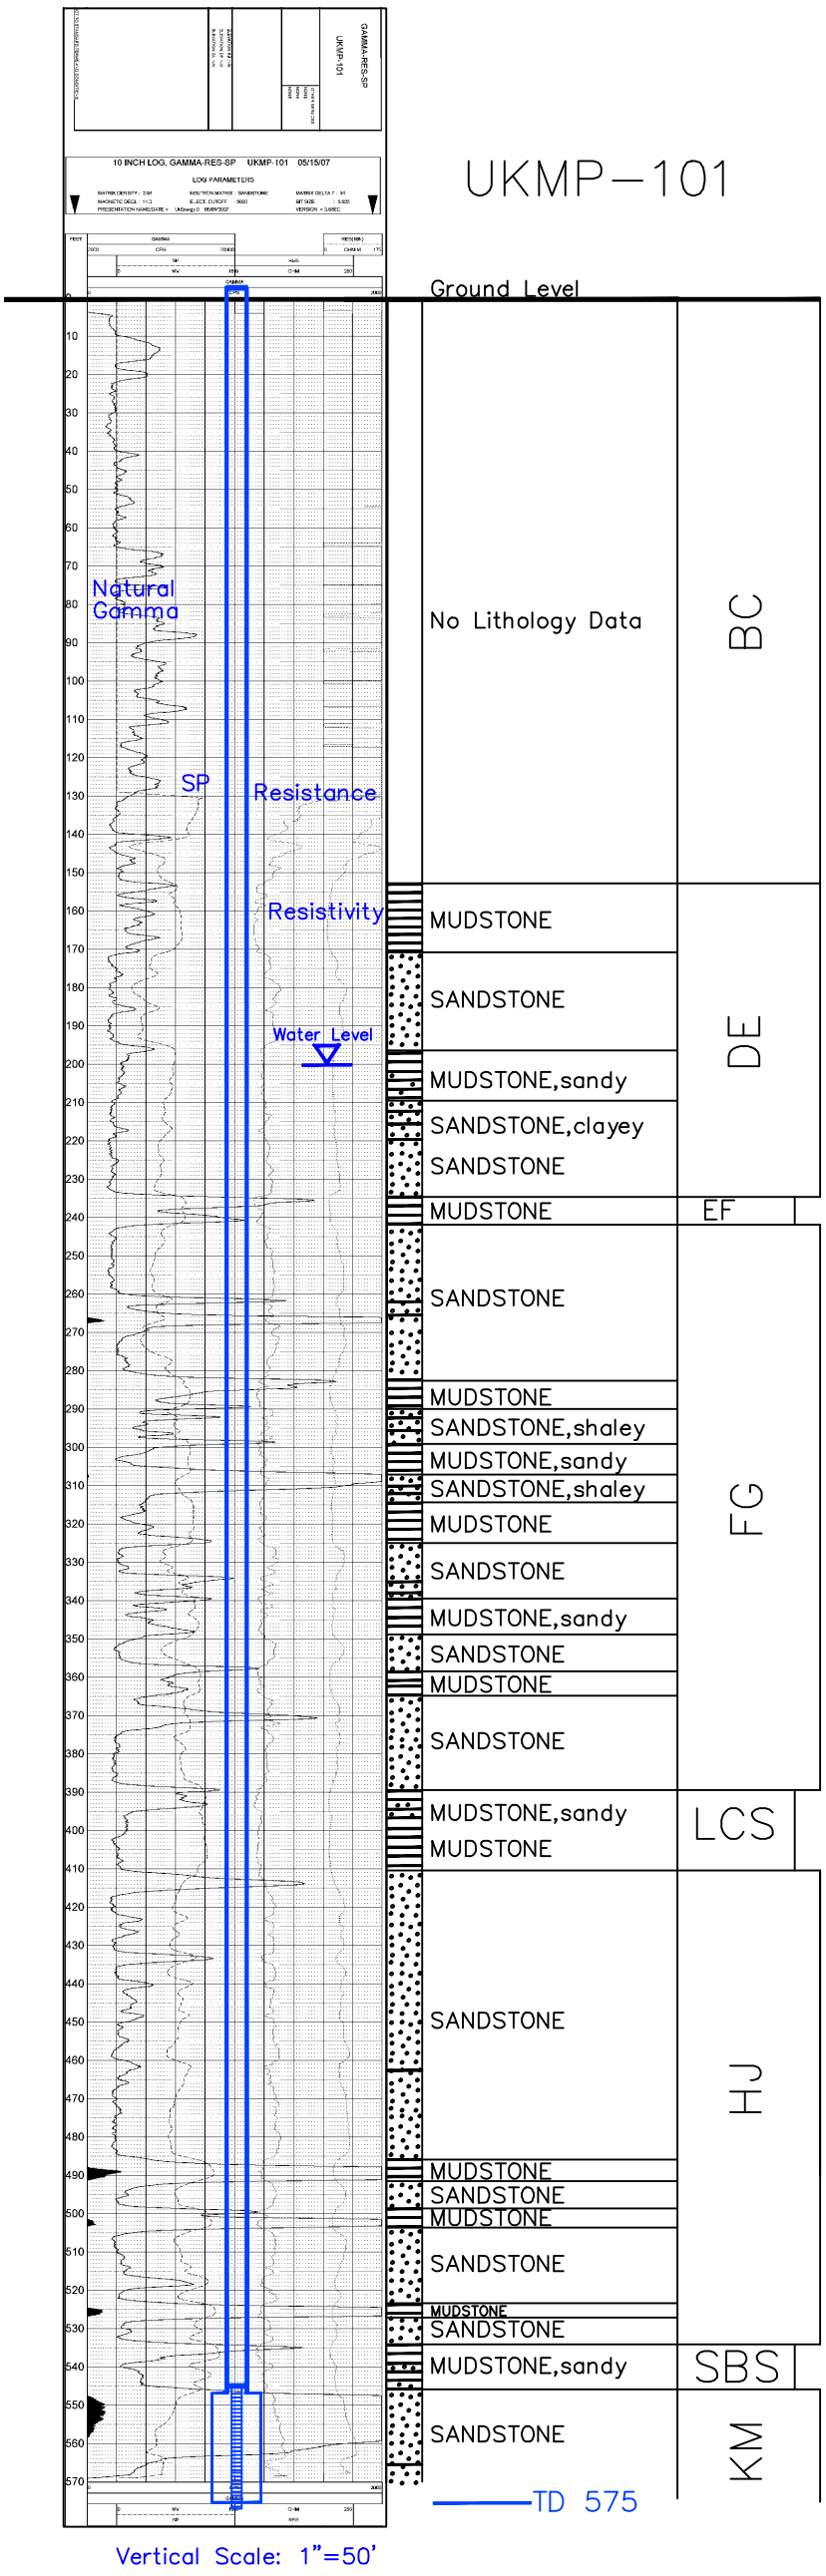

UKMP–101

Lost Creek ISR, LLC

WELL COMPLETION REPORT

WELL # UKMP–101 SEO # 179906 Date Drilled: 5–15–07

Location: E 744,090 / N 534,929 (NAD 27)

Ground Elev: 6940.18 Measure Point Elev: 6941.74

TD: 575 ft. Hole Dia.: 7–7/8"

CASED to: 547' Casing: PVC SDR17 ID: 4.5" OD: 5"

GROUT: Portland Cement – Type I/II
Pumped thru casing, displaced to surface with water

COMPLETION Aquifer: UKM Sand

Static Water Level: Depth 199' Elev: 6742' (avg.)

UNDERREAM: Blade Dia: 10–1/2"

Intervals: from 547' to 575' /length 28'

from _____ to _____ /length _____

SCREEN LINER ASSEMBLY

Description	Depth From	– To	/ Elev. From	– To	Length
K–packer		545'		6396'	
Screen	547'	577'	6394'	6364'	30'

SCREEN SPECIFICATIONS:

Slot: 0.020" Composition 3" PVC

FILTER PACKING:

Volume: _____ (bags)(ft^3) Sand Specs. _____

Method: N/A

WELL STIMULATION: Method Airlift

Yield: Good / (Moderate) / Poor
